

# *HMS, Inc.*

## HAZARD MANAGEMENT SERVICES, INC.

---

January 8, 2003

Mr. Rob Peters  
Chico Unified School District  
1163 E. Seventh Street  
Chico, CA 95928

Re: Asbestos Abatement Final Close-Out Documentation for the Pleasant Valley Senior High School, Portable T-1 Project

Dear Mr. Peters:

This letter reports the completion of the removal of asbestos-containing roofing materials. The project was completed in accordance with the abatement specifications included with this report. With this report Hazard Management Services, Inc. (HMS, Inc.) has completed all of our responsibilities under the present contract.

### **Asbestos Related Work**

Asbestos related work included removal of roofing material and mastic from the student restrooms building adjacent to Portable T-1. The abatement work was conducted by Janus Corporation and was completed on July 29, 2002.

Upon completion of the work, a thorough visual inspection was successfully conducted by HMS, Inc. No remaining dust or roofing debris was noted in the work areas or on the grounds surrounding this areas.

HMS, Inc. is including documentation provided by the contractor(s) with this report as part of the final close-out documentation, as required by the project specifications. These documents include copies of worker training certificates, medical exams, respirator fit tests, air sampling data, safety meetings, sign-in sheets, and other information that were submitted to HMS, Inc. HMS, Inc. cannot attest to the accuracy or validity of the documents provided by the contractor(s), since these were prepared by the contractor, not HMS, Inc. It is the responsibility of the contractor(s) to comply with the various regulations and provide valid, true, and accurate documents as they pertain to this project.

In order to meet the AHERA requirements, the enclosed documentation must be kept on file as part of the District's US EPA AHERA Management Plan. A copy of this report must be retained in the District Office and the appropriate school office. Be sure to update the list of asbestos-containing building materials in the Management Plan. Indicate on the "Homogeneous Material Records" (HMR) the abatement action taken. Also, be sure to note in the District's annual notifications to parents and employees that abatement work was completed at this site.

It has been our pleasure working with you on this project. If you desire any further services, or have questions, please call our Rocklin office at (916) 632-6800.

Sincerely,



Robert C. Howell  
Project Manager  
CAC# 92-0849

Enclosures

A:\R0747\RoofLtr.wpd

4200 Rocklin Rd., Ste. 11A  
Rocklin, CA 95677  
(916) 632-6800  
(916) 632-6841 Fax

367 Civic Drive, Ste. 7  
Pleasant Hill, CA 94523-1936  
(925) 363-3442  
(925) 363-7897 Fax

P.O. Box 576848  
Modesto, CA 95357-6848  
(209) 551-2000  
(209) 575-5657 Fax

371 E. Bullard Ave., Ste. 109  
Fresno, CA 93710-5217  
(559) 436-0277  
(559) 436-0279 Fax

4949 Buckley Way, #105  
Bakersfield, CA 93390-4880  
(661) 833-0351  
(661) 833-0361 Fax

# *HMS, Inc.*

## HAZARD MANAGEMENT SERVICES, INC.

---

January 8, 2003

Mr. Rob Peters  
Chico Unified School District  
1163 E. Seventh Street  
Chico, CA 95928

Re: Asbestos Abatement Final Close-Out Documentation for the Pleasant Valley Senior High School, Roof of Shop Building Project

Dear Mr. Peters:

This letter reports the completion of the removal of asbestos-containing roofing materials. The project was completed in accordance with the abatement specifications included with this report. With this report Hazard Management Services, Inc. (HMS, Inc.) has completed all of our responsibilities under the present contract.

### **Asbestos Related Work**

Asbestos related work included removal of roofing material and mastic from the shop building roof. The abatement work was conducted by Janus Corporation and was completed on June 22, 2002.

Upon completion of the work, a thorough visual inspection was successfully conducted by HMS, Inc. No remaining dust or roofing debris was noted in the work areas or on the grounds surrounding this areas.


Area air samples were collected by HMS, Inc. to monitor the work practices of the abatement contractor. The analytical results of these samples indicated the work practices utilized by the contractor were effective in controlling emissions during the removal work. All area samples were analyzed utilizing Phase Contrast Microscopy (PCM) in accordance with the NIOSH 7400 method by Asbestech of Carmichael, CA. A copy of laboratory certifications are included in the project documents.

HMS, Inc. is including documentation provided by the contractor(s) with this report as part of the final close-out documentation, as required by the project specifications. These documents include copies of worker training certificates, medical exams, respirator fit tests, air sampling data, safety meetings, sign-in sheets, and other information that were submitted to HMS, Inc. HMS, Inc. cannot attest to the accuracy or validity of the documents provided by the contractor(s), since these were prepared by the contractor, not HMS, Inc. It is the responsibility of the contractor(s) to comply with the various regulations and provide valid, true, and accurate documents as they pertain to this project.

In order to meet the AHERA requirements, the enclosed documentation must be kept on file as part of the District's US EPA AHERA Management Plan. A copy of this report must be retained in the District Office and the appropriate school office. Be sure to update the list of asbestos-containing building materials in the Management Plan. Indicate on the "Homogeneous Material Records" (HMR) the abatement action taken. Also, be sure to note in the District's annual notifications to parents and employees that abatement work was completed at this site.

It has been our pleasure working with you on this project. If you desire any further services, or have questions, please call our Rocklin office at (916) 632-6800.

Sincerely,



Cory R. Sanders  
Site Surveillance Technician  
SST # 91-2991

Enclosures

A:\R0726\FinalLtr.wpd

4200 Rocklin Rd., Ste. 11A  
Rocklin, CA 95677  
(916) 632-6800  
(916) 632-6841 Fax

367 Civic Drive, Ste. 7  
Pleasant Hill, CA 94523-1936  
(925) 363-3442  
(925) 363-7897 Fax

P.O. Box 576848  
Modesto, CA 95357-6848  
(209) 551-2000  
(209) 575-5657 Fax

371 E. Bullard Ave., Ste. 109  
Fresno, CA 93710-5217  
(559) 436-0277  
(559) 436-0279 Fax

4949 Buckley Way, #105  
Bakersfield, CA 93390-4880  
(661) 833-0351  
(661) 833-0361 Fax

## Chico Unified School District

This project has **two** numbers for Pleasant Valley Senior High School:

R0726	06/22/02	Roof of Shop Building	One Day Job
R0747	07/29/02	Portable T-1	One Day Job

This Section should contain the following items. Those that are (✓) must be added by the District/Owner.

## **II. CONTRACTOR DOCUMENTATION**

- ( ) Contractor License**
- ( ) DOSH Registration**
- ( ) Asbestos Certification**
- ( ) Contractor General Liability**
- ( ) Contractor Worker's Compensation**
- ( ) Contractor Automobile Insurance**
- (N/A) Contractor Bid Bond**
- (N/A) Contractor Performance Bond**
- (N/A) Contractor Payment Bond**
- (N/A) Contractor Contract Agreement or Purchase Order**
- (N/A) Subcontractor General Liability Insurance**
- (N/A) Subcontractor Worker's Compensation**
- (N/A) Subcontractor Automobile Insurance**
- ( ) APCD & AQMB**
- (N/A) EPA**
- ( ) DOSH**
- (N/A) ARB**
- (N/A) Project Schedule**



State of California  
CONTRACTORS STATE LICENSE BOARD  
ACTIVE LICENSE



License Number **572682**

Entity **CORP**

Business Name **JANUS CORPORATION**

Classification(s) **A ASB B C-2 HAZ HIC**

Expiration Date **07/31/2003**



Any change of business address/name must be reported to the Registrar within 90 days.

This license is not transferrable, and shall be returned to the Registrar  
upon demand when suspended, revoked or invalidated for any reason.  
This pocket card is valid through the expiration date only.

If found, drop in any mailbox.  
Postage guaranteed by  
Contractors State License Board  
P.O. Box 26000  
Sacramento, CA 95826


Licensee Signature

State of California

# Contractors State License Board

Pursuant to Chapter 9 of Division 3 of the Business and Professions Code  
and the Rules and Regulations of the Contractors State License Board,  
the Registrar of Contractors does hereby issue this license to:

JANUS CORPORATION



to engage in the business or act in the capacity of a contractor  
in the following classification(s):

- A - GENERAL ENGINEERING CONTRACTOR  
ASB - ASBESTOS
- B - GENERAL BUILDING CONTRACTOR
- C-2 - INSULATION AND ACOUSTICAL

Witness my hand and seal this day,

July 28, 1993

Issued July 11, 1989

CERTIFIED COPY

Signature of Licensee


Registrar of Contractors

572682

License Number

This license is the property of the Registrar of Contractors, is not  
transferable, and shall be returned to the Registrar upon demand  
when suspended, revoked, or invalidated for any reason. It becomes  
void if not renewed.

Signature of License Qualifier



*David R. Phillips*

STATE OF CALIFORNIA  
STATE AND CONSUMER SERVICES AGENCY

DEPARTMENT OF

**Consumer  
Affairs**

CONTRACTORS STATE LICENSE BOARD

*Building Quality*



**ASBESTOS**


**CERTIFICATION**

Pursuant to the provisions of Section 7058.5 of the Business and Professions Code, the Registrar of Contractors does hereby certify that the following qualifying person has successfully completed the asbestos certification examination:

Qualifier: **MICHAEL F. ELY**

License No.: **572682**

Namestyle: **JANUS CORPORATION**



WITNESS my hand and official seal this

**11th** day of **JULY, 1989**

*David R. Phillips*  
Registrar of Contractors

13L-35 (7/88)

This certification is the property of the Registrar of Contractors. It is not transferable, and shall be returned to the Registrar upon demand when suspended, revoked, or invalidated for any reason.

**A5181**

JUN-05-2002 15:16

P.01

State of California



Department of Industrial Relations


DIVISION OF OCCUPATIONAL SAFETY AND HEALTH

# Certificate of Registration for Asbestos-related Work

Certificate No. 224Expiration Date 10-Aug-02**JANUS CORPORATION**

(Name of Employer)

is duly registered by the Division of Occupational Safety and Health in accordance with the California Administrative Code, Title 8, Article 2.5 for asbestos-related work.

04-Jun-02  
Date of Issuance  
Chief, Division of Occupational Safety and HealthEffective Date 11-Aug-01Contractor's License No. 572682

This registration is valid only when the following requirements and conditions are met:

1. The registered employer shall safely perform asbestos-related work in compliance with relevant occupational safety and health regulations.
2. The registered employer shall notify the Division of changes in work locations or conditions as specified by Section 341.9 of Title 8 of the California Administrative Code.
3. The registered employer shall post a sign readable at 20 feet at the location of any asbestos-related work stating:

**Danger-Asbestos  
Cancer and Lung Hazard  
Authorized Personnel Only**

4. A copy of the registration shall be posted at the jobsite beside the Cal-OSHA poster.
5. The registered employer shall provide a copy of this registration certificate to the prime contractor and any other employers at the site before the commencement of any asbestos-related work.
6. The registered employer shall conduct a safety conference prior to the commencement of any asbestos-related work as specified by Section 341.11 of Title 8 of the California Administrative Code.
7. The registered employer acknowledges the Division's right to revoke or suspend this registration as provided by Section 341.14 of Title 8 of the California Administrative Code.



DEPARTMENT OF INDUSTRIAL RELATIONS  
DIVISION OF OCCUPATIONAL SAFETY AND HEALTHOccupational Carcinogen Control Unit  
455 Golden Gate Avenue, Room 5202  
San Francisco, CA 94102ADDRESS REPLY TO:  
P.O. BOX 420603  
San Francisco, CA 94142

October 3, 1994

JANUS CORPORATION  
3795 PACHECO BLVD., SUITE C  
MARTINEZ CA 94553CONFIRMATION OF REGISTRATION

Your carcinogen "Report of Use", or Cal/OSHA Form 183A, has been received and the carcinogen(s) checked has(have) been recorded with your assigned registration number and effective date below:

REGISTRATION NUMBER: 5493

EFFECTIVE DATE: 11/21/91

<u>CODE</u>	<u>CARCINOGEN</u>	<u>SECTION</u>	<u>INDIVIDUAL</u>
015	Asbestos	1529, 5208, 5208.1	November 21, 1991

KEEP THIS DOCUMENT AS A RECORD OF YOUR REPORT.  
PLEASE ADVISE THIS OFFICE OF CHANGES TO YOUR REPORT OF USE  
WITHIN 15 CALENDAR DAYS PER THE CALIFORNIA CODE OF REGULA-  
TIONS, TITLE 8, SECTIONS AS LISTED.

FOR FURTHER ASSISTANCE CALL (415) 703-5301, OCCUPATIONAL CARCINOGEN CONTROL UNIT.

CC: Barbara G. Eaves, Office Mgr  
Per your ltr dtd 10/7/94 your address and phone number change has  
been registered.)

Cal/OSHA 183C  
May 1994

Client#: 3145

JANUSCORP1

# ACORD CERTIFICATE OF LIABILITY INSURANCE

DATE (MM/DD/YY)  
04/13/02

PRODUCER  
ley, Renton & Associates  
Box 12675  
kland, CA 94604-2675  
510 465-3090

THIS CERTIFICATE IS ISSUED AS A MATTER OF INFORMATION ONLY AND CONFERS NO RIGHTS UPON THE CERTIFICATE HOLDER. THIS CERTIFICATE DOES NOT AMEND, EXTEND OR ALTER THE COVERAGE AFFORDED BY THE POLICIES BELOW.

## INSURERS AFFORDING COVERAGE

INSURED  
Janus Corporation  
1081 Shary Circle  
Concord, CA 94518

INSURER A: Zurich American Insurance Co.  
INSURER B: American Guarantee & Liability  
INSURER C: State Compensation Ins. Fund of CA  
INSURER D: Steadfast Ins. Co.  
INSURER E:

## COVERAGES

THE POLICIES OF INSURANCE LISTED BELOW HAVE BEEN ISSUED TO THE INSURED NAMED ABOVE FOR THE POLICY PERIOD INDICATED. NOTWITHSTANDING ANY REQUIREMENT, TERM OR CONDITION OF ANY CONTRACT OR OTHER DOCUMENT WITH RESPECT TO WHICH THIS CERTIFICATE MAY BE ISSUED OR MAY PERTAIN, THE INSURANCE AFFORDED BY THE POLICIES DESCRIBED HEREIN IS SUBJECT TO ALL THE TERMS, EXCLUSIONS AND CONDITIONS OF SUCH POLICIES. AGGREGATE LIMITS SHOWN MAY HAVE BEEN REDUCED BY PAID CLAIMS.

INSR LTR	TYPE OF INSURANCE	POLICY NUMBER	POLICY EFFECTIVE DATE (MM/DD/YY)	POLICY EXPIRATION DATE (MM/DD/YY)	LIMITS
A	GENERAL LIABILITY	GLO521873100	07/01/01	07/01/02	EACH OCCURRENCE \$5,000,000
	<input checked="" type="checkbox"/> COMMERCIAL GENERAL LIABILITY				FIRE DAMAGE (Any one fire) \$100,000
	<input type="checkbox"/> CLAIMS MADE <input checked="" type="checkbox"/> OCCUR				MED EXP (Any one person) \$5,000
					PERSONAL & ADV INJURY \$5,000,000
					GENERAL AGGREGATE \$5,000,000
					PRODUCTS - COMP/OP AGG \$5,000,000
	GEN'L AGGREGATE LIMIT APPLIES PER: <input type="checkbox"/> POLICY <input checked="" type="checkbox"/> PRO-JECT <input type="checkbox"/> LOC				
B	AUTOMOBILE LIABILITY	BAP377647202	07/01/01	07/01/02	COMBINED SINGLE LIMIT (Ea accident) \$2,000,000
	<input checked="" type="checkbox"/> ANY AUTO				BODILY INJURY (Per person) \$
	<input type="checkbox"/> ALL OWNED AUTOS				BODILY INJURY (Per accident) \$
	<input type="checkbox"/> SCHEDULED AUTOS				PROPERTY DAMAGE (Per accident) \$
	<input type="checkbox"/> HIRBD AUTOS				
	<input type="checkbox"/> NON-OWNED AUTOS				
	GARAGE LIABILITY				AUTO ONLY - BA ACCIDENT \$
	<input type="checkbox"/> ANY AUTO				OTHER THAN BA ACC \$
					AUTO ONLY: AGG \$
	EXCESS LIABILITY				EACH OCCURRENCE \$
	<input type="checkbox"/> OCCUR <input type="checkbox"/> CLAIMS MADE				AGGREGATE \$
	<input type="checkbox"/> DEDUCTIBLE				\$
	<input type="checkbox"/> RETENTION \$				\$
C	WORKERS COMPENSATION AND EMPLOYERS' LIABILITY	1633736	07/01/01	07/01/02	<input checked="" type="checkbox"/> WC STATU-TORY LIMITS <input type="checkbox"/> OTH-BK
					E.L. EACH ACCIDENT \$1,000,000
					E.L. DISEASE - BA EMPLOYEE \$1,000,000
					E.L. DISEASE - POLICY LIMIT \$1,000,000
D	OTHER Contractors	CPL522026500	07/01/01	07/01/02	\$5,000,000 each loss
	Pollution Liability				\$5,000,000 all losses

DESCRIPTION OF OPERATIONS/LOCATIONS/VEHICLES/EXCLUSIONS ADDED BY ENDORSEMENT/SPECIAL PROVISIONS

Job #02-107, The certificate holder & HMS, Inc. are named as an additional insured as respects general liability for claims arising from the operations of the named insured.

CERTIFICATE HOLDER

ADDITIONAL INSURED; INSURER LETTER

## CANCELLATION Ten Day Notice for Non-Payment of Premium

Chico Unified  
School District  
1163 East 4th Street  
Chico, CA 95928

SHOULD ANY OF THE ABOVE DESCRIBED POLICIES BE CANCELLED BEFORE THE EXPIRATION DATE THEREOF, THE ISSUING INSURER WILL ENDEAVOR TO MAIL 30 DAYS WRITTEN NOTICE TO THE CERTIFICATE HOLDER NAMED TO THE LEFT, BUT FAILURE TO DO SO SHALL IMPOSE NO OBLIGATION OR LIABILITY OF ANY KIND UPON THE INSURER, ITS AGENTS OR REPRESENTATIVES.

AUTHORIZED REPRESENTATIVE

Steve B. Baker

ACORD

## CERTIFICATE OF LIABILITY INSURANCE

DATE (MM/DD/YY)  
06/20/02

## PRODUCER

Dealey, Renton & Associates  
P.O. Box 12675  
Oakland, CA 94604-2675  
510 465-3090

THIS CERTIFICATE IS ISSUED AS A MATTER OF INFORMATION ONLY AND CONFERS NO RIGHTS UPON THE CERTIFICATE HOLDER. THIS CERTIFICATE DOES NOT AMEND, EXTEND OR ALTER THE COVERAGE AFFORDED BY THE POLICIES BELOW.

## INSURERS AFFORDING COVERAGE

## INSURED

Janus Corporation  
1081 Shary Circle  
Concord, CA 94518

INSURER A: Zurich American Insurance Co.

INSURER B: American Guarantee &amp; Liability

INSURER C: State Compensation Ins. Fund of CA

INSURER D: Steadfast Ins. Co.

INSURER E:

## COVERAGES

THE POLICIES OF INSURANCE LISTED BELOW HAVE BEEN ISSUED TO THE INSURED NAMED ABOVE FOR THE POLICY PERIOD INDICATED. NOTWITHSTANDING ANY REQUIREMENT, TERM OR CONDITION OF ANY CONTRACT OR OTHER DOCUMENT WITH RESPECT TO WHICH THIS CERTIFICATE MAY BE ISSUED OR MAY PERTAIN, THE INSURANCE AFFORDED BY THE POLICIES DESCRIBED HEREIN IS SUBJECT TO ALL THE TERMS, EXCLUSIONS AND CONDITIONS OF SUCH POLICIES. AGGREGATE LIMITS SHOWN MAY HAVE BEEN REDUCED BY PAID CLAIMS.

NSR LTR	TYPE OF INSURANCE	POLICY NUMBER	POLICY EFFECTIVE DATE (MM/DD/YY)	POLICY EXPIRATION DATE (MM/DD/YY)	LIMITS
A	GENERAL LIABILITY	GLO521873100	07/01/01	07/01/02	EACH OCCURRENCE \$5,000,000
	<input checked="" type="checkbox"/> COMMERCIAL GENERAL LIABILITY				FIRE DAMAGE (Any one fire) \$100,000
	<input type="checkbox"/> CLAIMS MADE <input checked="" type="checkbox"/> OCCUR				MED EXP (Any one person) \$5,000
					PERSONAL & ADV INJURY \$5,000,000
					GENERAL AGGREGATE \$5,000,000
					PRODUCTS-COMP/OP AGG \$5,000,000
	GEN'L AGGREGATE LIMIT APPLIES PER:				
	<input type="checkbox"/> POLICY <input checked="" type="checkbox"/> PRO- JECT <input type="checkbox"/> LOC				
B	AUTOMOBILE LIABILITY	BAP377647202	07/01/01	07/01/02	COMBINED SINGLE LIMIT (Ea accident) \$2,000,000
	<input checked="" type="checkbox"/> ANY AUTO				BODILY INJURY (Per person) \$
	<input type="checkbox"/> ALL OWNED AUTOS				BODILY INJURY (Per accident) \$
	<input type="checkbox"/> SCHEDULED AUTOS				PROPERTY DAMAGE (Per accident) \$
	<input type="checkbox"/> HIRED AUTOS				
	<input type="checkbox"/> NON-OWNED AUTOS				
	GARAGE LIABILITY				AUTO ONLY - EA ACCIDENT \$
	<input type="checkbox"/> ANY AUTO				OTHER THAN EA ACC \$
					AUTO ONLY: AGG \$
	EXCESS LIABILITY				EACH OCCURRENCE \$
	<input type="checkbox"/> OCCUR <input type="checkbox"/> CLAIMS MADE				AGGREGATE \$
					\$
	DEDUCTIBLE				\$
	RETENTION \$				\$
C	WORKERS COMPENSATION AND EMPLOYERS' LIABILITY	1633736	07/01/01	07/01/02	<input checked="" type="checkbox"/> WC STATU- TORY LIMITS <input type="checkbox"/> OTH- ER
					E.L. EACH ACCIDENT \$1,000,000
					E.L. DISEASE-EA EMPLOYEE \$1,000,000
					E.L. DISEASE-POLICY LIMIT \$1,000,000
D	OTHER Contractors	CPL522026500	07/01/01	07/01/02	\$5,000,000 each loss
	Pollution				\$5,000,000 all losses
	Liability				

## DESCRIPTION OF OPERATIONS/LOCATIONS/VEHICLES/EXCLUSIONS ADDED BY ENDORSEMENT/SPECIAL PROVISIONS

Job #02-219, The certificate holder is named as an additional insured as respects general liability for claims arising from the operations of the named insured.

## CERTIFICATE HOLDER


ADDITIONAL INSURED; INSURER LETTER: \_\_\_\_\_

## CANCELLATION Ten Day Notice for Non-Payment of Premium

Chico Unified  
School District  
1163 East 4th Street  
Chico, CA 95928

SHOULD ANY OF THE ABOVE DESCRIBED POLICIES BE CANCELLED BEFORE THE EXPIRATION DATE THEREOF, THE ISSUING INSURER WILL ENDEAVOR TO MAIL 30 DAYS WRITTEN NOTICE TO THE CERTIFICATE HOLDER NAMED TO THE LEFT, BUT FAILURE TO DO SO SHALL IMPOSE NO OBLIGATION OR LIABILITY OF ANY KIND UPON THE INSURER, ITS AGENTS OR REPRESENTATIVES.

AUTHORIZED REPRESENTATIVE



**ACORD****CERTIFICATE OF LIABILITY INSURANCE**DATE (MM/DD/YY)  
07/01/02**PRODUCER**Dealey, Renton & Associates  
P.O. Box 12675  
Concord, CA 94604-2675  
510 465-3090

THIS CERTIFICATE IS ISSUED AS A MATTER OF INFORMATION ONLY AND CONFERS NO RIGHTS UPON THE CERTIFICATE HOLDER. THIS CERTIFICATE DOES NOT AMEND, EXTEND OR ALTER THE COVERAGE AFFORDED BY THE POLICIES BELOW.

**INSURERS AFFORDING COVERAGE****INSURED**Janus Corporation  
1081 Shary Circle  
Concord, CA 94518

INSURER A: Zurich American Insurance Co.

INSURER B: American Guarantee &amp; Liability

INSURER C: State Compensation Ins. Fund of CA

INSURER D: Steadfast Ins. Co.

INSURER E:

**COVERAGES**

THE POLICIES OF INSURANCE LISTED BELOW HAVE BEEN ISSUED TO THE INSURED NAMED ABOVE FOR THE POLICY PERIOD INDICATED. NOTWITHSTANDING ANY REQUIREMENT, TERM OR CONDITION OF ANY CONTRACT OR OTHER DOCUMENT WITH RESPECT TO WHICH THIS CERTIFICATE MAY BE ISSUED OR MAY PERTAIN, THE INSURANCE AFFORDED BY THE POLICIES DESCRIBED HEREIN IS SUBJECT TO ALL THE TERMS, EXCLUSIONS AND CONDITIONS OF SUCH POLICIES. AGGREGATE LIMITS SHOWN MAY HAVE BEEN REDUCED BY PAID CLAIMS.

INSR LTR	TYPE OF INSURANCE	POLICY NUMBER	POLICY EFFECTIVE DATE (MM/DD/YY)	POLICY EXPIRATION DATE (MM/DD/YY)	LIMITS
A	GENERAL LIABILITY	GLO521873101	07/01/02	07/01/03	EACH OCCURRENCE \$5,000,000
	<input checked="" type="checkbox"/> COMMERCIAL GENERAL LIABILITY				FIRE DAMAGE (Any one fire) \$100,000
	<input type="checkbox"/> CLAIMS MADE <input checked="" type="checkbox"/> OCCUR				MED EXP (Any one person) \$5,000
					PERSONAL & ADV INJURY \$5,000,000
					GENERAL AGGREGATE \$5,000,000
					PRODUCTS-COMP/OP AGG \$5,000,000
	GENL AGGREGATE LIMIT APPLIES PER:				
	<input type="checkbox"/> POLICY <input checked="" type="checkbox"/> PROJECT <input type="checkbox"/> LOC				
B	AUTOMOBILE LIABILITY	BAP377647203	07/01/02	07/01/03	COMBINED SINGLE LIMIT (Ea accident) \$2,000,000
	<input checked="" type="checkbox"/> ANY AUTO				BODILY INJURY (Per person) \$
	<input type="checkbox"/> ALL OWNED AUTOS				BODILY INJURY (Per accident) \$
	<input type="checkbox"/> SCHEDULED AUTOS				PROPERTY DAMAGE (Per accident) \$
	<input type="checkbox"/> HIRED AUTOS				
	<input type="checkbox"/> NON-OWNED AUTOS				
	GARAGE LIABILITY				AUTO ONLY - EA ACCIDENT \$
	<input type="checkbox"/> ANY AUTO				OTHER THAN EA ACC \$
					AUTO ONLY: AGG \$
	EXCESS LIABILITY				EACH OCCURRENCE \$
	<input type="checkbox"/> OCCUR <input type="checkbox"/> CLAIMS MADE				AGGREGATE \$
	<input type="checkbox"/> DEDUCTIBLE				\$
	<input type="checkbox"/> RETENTION \$				\$
C	WORKERS COMPENSATION AND EMPLOYERS' LIABILITY	163373602	07/01/02	07/01/03	<input checked="" type="checkbox"/> WC STATU-TORY LIMITS <input type="checkbox"/> OTHER \$
					E.L. EACH ACCIDENT \$1,000,000
					E.L. DISEASE-EA EMPLOYEE \$1,000,000
					E.L. DISEASE-POLICY LIMIT \$1,000,000
D	OTHER Contractors Pollution Liability	CPL522026501	07/01/02	07/01/03	\$5,000,000 each loss \$5,000,000 all losses

**DESCRIPTION OF OPERATIONS/LOCATIONS/VEHICLES/EXCLUSIONS ADDED BY ENDORSEMENT/SPECIAL PROVISIONS**

Job #02-107, The certificate holder &amp; HMS, Inc. are named as an additional insured as respects general liability for claims arising from the operations of the named insured.

**CERTIFICATE HOLDER**

ADDITIONAL INSURED; INSURER LETTER:

**CANCELLATION Ten Day Notice for Non-Payment of Premium**Chico Unified  
School District  
1163 East 4th Street  
Chico, CA 95928

SHOULD ANY OF THE ABOVE DESCRIBED POLICIES BE CANCELLED BEFORE THE EXPIRATION DATE THEREOF, THE ISSUING INSURER WILL ENDEAVOR TO MAIL 30 DAYS WRITTEN NOTICE TO THE CERTIFICATE HOLDER NAMED TO THE LEFT, BUT FAILURE TO DO SO SHALL IMPOSE NO OBLIGATION OR LIABILITY OF ANY KIND UPON THE INSURER, ITS AGENTS OR REPRESENTATIVES.

AUTHORIZED REPRESENTATIVE

*Stefano B. D.*

POLICY NUMBER: GLO521873101

COMMERCIAL GENERAL LIABILITY  
CG 20 10 10 93

THIS ENDORSEMENT CHANGES THE POLICY. PLEASE READ IT CAREFULLY.

## **ADDITIONAL INSURED - OWNERS, LESSEES or CONTRACTORS FORM B**

This endorsement modifies insurance provided under the following:

COMMERCIAL GENERAL LIABILITY COVERAGE PART

### **SCHEDULE**

Name of Person or Organization:

Chico Unified  
School District  
1163 East 4th Street  
Chico, CA 95928

(If no entry appears above, information required to complete this endorsement will be shown in the Declarations as applicable to this endorsement.)

WHO IS AN INSURED (Section II) is amended to include as an insured the person or organization shown in the Schedule, but only with respect to liability arising out of your ongoing operations performed for that insured.

Job #02-107, The certificate holder & HMS, Inc. are named as an additional insured as respects general liability for claims arising from the operations of the named insured.

TEMPORARY WORKSITE NOTIFICATION FOR ASBESTOS  
and METHYLENEDIANILINE-RELATED WORK

DATE OF  
NOTIFICATION: 13-Jun-02  
COMPANY: JANUS CORPORATION, (925) 969-9200

REVISION #  
DATE OF REVISION

COMPANY/EMPLOYER NAME: CHICO UNIFIED SCHOOL DISTRICT  
HEADQUARTERS ADDRESS: 1163 EAST 4TH ST CHICO, CA 95928

\*CONTRACTORS STATE LICENSE BOARD LICENSE NUMBER: 572682  
DOSH-OCCU (CAL/OSHA) \*ASBESTOS REGISTRATION NUMBER: 224  
and/or "REPORT OF USE" REGISTRY NUMBER: \_\_\_\_\_

ADDRESS OF TEMPORARY WORKSITE and PRECISE LOCATION:  
1475 EAST AVE CHICO 95926

BUILDING E AUTO SHOP ROOF

NEAREST INTERSECTION: MAGNOLIA

TYPE OF BUSINESS: SCHOOL

\*NAME OF CERTIFIED SUPERVISOR: ARMONDO DEL TORO

\*NAME OF QUALIFIED PERSON IN CHARGE OF AIR MONITORING,  
LABORATORY WORK, AND RESPIRATORS: ARMONDO DEL TORO

\*NAME OF CERTIFIED CONSULTANT: HMS.INC

PROJECTED JOB STARTING DATE: 22-Jun-02 PROJ. COMPLETION DATE: 23-Jun-02

DESCRIBE TYPE, SCOPE AND WORK PRACTICES OF JOB:

ROOFING

Neg. air, wet methods, full containment.

EVALUATION OF POTENTIAL FOR EXPOSURE: LOW

ESTIMATED NUMBER OF EMPLOYEES ON THIS JOB: 6

ACCORDING TO TITLE 8 CCR SECTIONS 341.9 AND 1529(r) for ASBESTOS and 5200(p) for MDA, PLEASE  
SEND THIS COMPLETED NOTICE TO THE NEAREST DISTRICT COMPLIANCE OFFICE (SEE  
ATTACHED LISTING), NOT TO DOSH HEADQUARTERS OR TO DOSH CONSULTATION, PRIOR TO  
COMMENCEMENT OF ANY SUCH WORK ACTIVITY.

NOTE: ANY CHANGE IN THE INFORMATION PROVIDED TO THE DISTRICT OFFICE BY THE  
WRITTEN NOTICE SHALL BE REPORTED TO THE DISTRICT OFFICE WITHIN 24 HOURS OF  
SUCH CHANGE.

\* The star denotes asbestos inquiry only

DOSH OFFICE NOTIFIED:

CAL/OSHA 183B

May, 1993

\_\_\_\_\_  
address/city/state/zip

\_\_\_\_\_  
phone

\_\_\_\_\_  
fax

JOB #: **02-219**

TEMPORARY WORKSITE NOTIFICATION FOR ASBESTOS  
and METHYLENEDIANILINE-RELATED WORK

DATE OF NOTIFICATION: 16-Jul-02  
COMPANY: JANUS CORPORATION, (925) 969-9200

REVISION #  
DATE OF REVISION

COMPANY/EMPLOYER NAME: CHICO UNIFIED SCHOOL DISTRICT  
HEADQUARTERS ADDRESS: 1163 EAST 4TH ST. CHICO, CA 95928

\*CONTRACTORS STATE LICENSE BOARD LICENSE NUMBER: 572682  
DOSH-OSCU (CAL/OSHA) \*ASBESTOS REGISTRATION NUMBER: 224  
and/or "REPORT OF USE" REGISTRY NUMBER: \_\_\_\_\_

ADDRESS OF TEMPORARY WORKSITE and PRECISE LOCATION:  
1475 EAST AVE CHICO CA 95926

RESTROOM ROOF

NEAREST INTERSECTION: MAGNOLA  
TYPE OF BUSINESS: SCHOOL

\*NAME OF CERTIFIED SUPERVISOR: JOSE SANDOVAL

\*NAME OF QUALIFIED PERSON IN CHARGE OF AIR MONITORING,  
LABORATORY WORK, AND RESPIRATORS: JOSE SANDOVAL

\*NAME OF CERTIFIED CONSULTANT: HMS, INC.

PROJECTED JOB STARTING DATE: 29-Jul-02 PROJ. COMPLETION DATE: 29-Jul-02

DESCRIBE TYPE, SCOPE AND WORK PRACTICES OF JOB:

ROOFING

Neg. air, wet methods, full containment.

EVALUATION OF POTENTIAL FOR EXPOSURE: LOW

ESTIMATED NUMBER OF EMPLOYEES ON THIS JOB: 4

ACCORDING TO TITLE 8 CCR SECTIONS 341.9 AND 1529(r) for ASBESTOS and 5200(p) for MDA, PLEASE  
SEND THIS COMPLETED NOTICE TO THE NEAREST DISTRICT COMPLIANCE OFFICE (SEE  
ATTACHED LISTING), NOT TO DOSH HEADQUARTERS OR TO DOSH CONSULTATION, PRIOR TO  
COMMENCEMENT OF ANY SUCH WORK ACTIVITY.

NOTE: ANY CHANGE IN THE INFORMATION PROVIDED TO THE DISTRICT OFFICE BY THE  
WRITTEN NOTICE SHALL BE REPORTED TO THE DISTRICT OFFICE WITHIN 24 HOURS OF  
SUCH CHANGE.

\* The star denotes asbestos inquiry only

CAL/OSHA 183B

DOSH OFFICE NOTIFIED: \_\_\_\_\_

May, 1993

address/city/state/zip

phone

fax

JOB #: **02-260**



**JANUS**  
CORPORATION

1081 SHARY CIRCLE  
CONCORD, CA 94518-2407  
(925) 969-9200  
FAX (925) 969-9290

- 1- There were no accidents reports on this job.
- 2- No notification of BAAQ on this job.
- 3- No DOP testing on this job.
- 4- No Manometer graphs reading need on this job.

*Craig M. Uhle*  
V. P. - Operations



TASK	APRIL							MAY													
	15	16	17	18	19	22	23	24	25	26	29	30	1	2							
PORTICO																					
prep	X	X																			
abate		X	X																		
detail				X																	
inspection					X																
VENT SHAFTS																					
prep	X	X																			
abate		X	X																		
detail				X																	
inspection					X																
ROOFING																					
prep													X								
abate													X	X		X					
detail																	X	X			
inspection																		X	X		



1081 SHARY CIRCLE  
CONCORD, CA 94518-2407  
(925) 969-9200  
FAX (925) 969-9290

April 10, 2002

Chico Unified School District  
1163 East 4<sup>th</sup> Street  
Chico, Ca. 95928

Project: CHICO HIGH SCHOOL GYMNASIUM ROOFING REMOVAL

Subject: Submittal Statements

Item 7. Janus will not be using any subcontractors on the project.

Item 11. Parking and city permits are not required on this project. Dumpsters will be on school property.

Item 12. Janus will not be renting any equipment.

Item 20. Personal air monitoring will be performed by Janus Corporation

**This section should contain the following items. Those that are checked (✓) must be added by the District/Owner.**

### **III. PRE-START MEETING DOCUMENTATION**

- ( ) Pre-Construction Meeting Documentation**
- ( ) Bidwalk Attendance**
- ( ) Results**
- ( ) Emergency Telephone Lists**

**This section should contain the following items. Those that are checked (✓) must be added by the District/Owner.**

#### **IV. CONTRACTOR EMPLOYEE RECORDS**

- ( ) Roster of Asbestos Workers**
- ( ) AHERA Training Certificates**
- ( ) Medical Monitoring Documentation**
- ( ) Respiratory Fit-Tests**

## WORKER'S NAMES & DATES

WORKER NAME and SOCIAL SECURITY NUMBER	Date 06/22/02	Worker Doc's Complete	Training Certificate Expires	Super- visor Yes/No	Date Medical Expires	Date Half Face Fit Test Expires
Juan Avalos	YES	YES	7/13/03	NO	12/7/02	11/7/02
Jorge Cervantes	YES	YES	5/11/03	NO	3/3/03	9/14/02
Armando Del Toro	YES	YES	5/4/03	NO	6/3/03	6/3/03
Marcos Del Toro	YES	YES	12/8/02	NO	10/5/03	5/22/03
Antonio Del Toro	YES	YES	9/8/02	NO	7/24/02	6/3/03
Raymundo Huerta	YES	YES	7/14/02	NO	7/26/02	6/10/03
Miguel Lopez	YES	YES	3/23/03	YES	5/23/03	4/10/03
Saul Lupian	YES	YES	3/9/03	NO	6/7/03	4/10/03
Rafael Lupian	YES	YES	7/26/02	NO	7/27/02	6/12/03
Nelson Magana	YES	YES	1/18/03	YES	2/8/03	7/23/02
Pedro Martinez	YES	YES	6/1/03	NO	3/15/03	4/10/03
Miguel Rodriguez	YES	YES	1/18/03	YES	12/10/02	4/8/03
Armando Rodriguez	YES	YES	3/23/03	YES	1/18/03	4/8/03
Javier Valdez	YES	YES	3/9/03	NO	10/12/02	4/8/03
Gerardo Valencia	YES	YES	5/31/03	NO	5/23/03	5/28/03

A:\WorkNms&Dat.wpd

# WORKER'S NAMES & DATES

## PORTABLE T-1 RESTROOM ROOF R0747

WORKER NAME and SOCIAL SECURITY NUMBER	Date 07/29/02	Worker Doc's Complete	Training Certificate Expires	Super- visor Yes/No	Date Medical Expires	Date Half Face Fit Test Expires
GARCIA, ABEL M 555-29-4631	YES	YES	04/27/03	NO	07/09/03	06/13/03
LOPEZ, MIGUEL GARCIA 622-92-5482	YES	YES	3/23/03	YES	5/23/03	4/10/03
OSEGUERA, SERGIO 617-18-6365	YES	YES	06/06/03	NO	06/05/02	03/10/03
RAZO, JOSE LUIS 622-94-0376	YES	YES	03/10/03	YES	09/13/03	11/29/03

A:\R0747\WorkNms&Dat\R0747.wpd

R0747

PORTABLE T-1

07/29/02

# WORKER'S NAMES & DATES

## PORTABLE T-1 RESTROOM ROOF R0747

WORKER NAME and SOCIAL SECURITY NUMBER	Date 07/29/02	Worker Doc's Complete	Training Certificate Expires	Super- visor Yes/No	Date Medical Expires	Date Half Face Fit Test Expires
GARCIA, ABEL M 555-29-4631	YES	YES	04/27/03	NO	07/09/03	06/13/03
LOPEZ, MIGUEL GARCIA 622-92-5482	YES	YES	3/23/03	YES	5/23/03	4/10/03
OSEGUERA, SERGIO 617-18-6365	YES	YES	06/06/03	NO	06/05/02	03/10/03
RAZO, JOSE LUIS 622-94-0376	YES	YES	03/10/03	YES	09/13/03	11/29/03

A:\R0747\WorkNms&Dat.R0747.wpd



**This section should contain the following items. Those that are checked (✓) must be added by the District/Owner.**

## **V. HMS, INC. DOCUMENTATION**

- ( ) Project Manager's Daily Log**
- ( ) Daily Laboratory Analysis Results**
- ( ) Daily Air Sample Submittals**
- ( ) Clearance Air Sample Results**
- ( ) Clearance Air Sample Submittals**
- ( ) Bulk Sample Results**
- ( ) Bulk Sample Submittals**
- ( ) Visual Inspection Report**
- (N/A) Attic Space Report**
- ( ) Rotameter Calibration Data**
- ( ) Laboratory Accreditation Statements (NVLAP, PAT)**
- ( ) AHERA & OSHA Documentation**

**HAZARD MANAGEMENT SERVICES, INC.  
SITE REPRESENTATIVE'S DAILY LOG**

**Client:** Chico USD  
**Project:** Pleasant Valley Senior High School  
Shop Building Roof Project

**Contact:** Rob Peters  
**Contact Phone:**  
**Contact Fax:**

**Project Number:** R0726

**Date:** 06/22/02      **Day:** Saturday      **Site Representative:** Cory Sanders

**Abatement Contractor:** Janus Corporation  
**Abatement Supervisor:** Nelson Magana

**Contractor Phone:** (925) 969-9200  
**Contractor FAX:** (925) 969-9290

**Samples Collected:**      TEM - N/A      PCM - 2 DA      PLM - N/A      Other - N/A

**Number of Abatement Personnel:** 14+ 1 supervisor

**Start Time:** 08:00 hrs.      **End Time:** 12:15 hrs.      **No. & Type of Waste Container(s):** 1 end dump

**Scope Of Work:** Removal of asbestos containing roofing materials from the shop building roof.

08:00 hrs. - I have arrived at the school. The abatement crew has not arrived yet, but Rob Peters is present. Rob has explained to me that the only roofing that will be abated today consists of an approximate three foot strip along the entire perimeter of the roof. This is the asbestos containing portion of the roof. Janus Corporation will be the abatement company performing the work today.


08:30 hrs. - Janus has arrived as well as the waste hauler. The hauler has positioned his trailer perpendicular to the building, making it easy for the workers to discard the waste. The trailer is on the east side of the building. Nelson Magana, the supervisor for Janus, has handed me worker documentation for the crew performing abatement today. Barrier tape is being strung creating a regulated area that only authorized individuals may breach. All workers are donning protective full body coveralls, work boots, and HEPA filtered respirators. The pre-start visual inspection has passed.

09:00 hrs.- There are 14 workers here today to perform a relatively small amount of removal. The ACM being removed extends from the roof edge to approx. three feet in from the roof edge. I have started a daily air sample on the east side of the shop building next to the waste bin.

09:15 hrs.- I have stated a second daily air sample on the east side of the shop building next to the entrance gate.

10:00 hrs.- The workers are removing the roofing materials quickly with metal bladed hand tools. One worker is using a garden hose to apply water to the waste bin area. This is helping keep dust suppressed while the debris is being discarded. Work should be done by approx. 12:00 noon.

11:00 hrs. - Workers have completed 3/4 of the work. They are cleaning as they go, leaving only the wood substrate. The substrate is solid, so no interior contamination of the building should occur. Rob Peters and I have both walked through the shop building making sure everything is as it should be.



Signature of Site Representative

**HAZARD MANAGEMENT SERVICES, INC.  
SITE REPRESENTATIVE'S DAILY LOG**

**Client:** Chico USD

**Project:** Pleasant Valley Senior High School  
Shop Building Roof Project

**Contact:** Rob Peters

**Contact Phone:**

**Contact Fax:**

**Project Number:** R0726

**Date:** 06/22/02

**Day:** Saturday

**Site Representative:** Cory Sanders

12:00 hrs. - Workers have completed the removal work. I have walked the roof perimeter visually inspecting for any missed debris. Janus has done clean work.

12:15 hrs. - The final visual inspection of the roof edge has passed. Rob Peters and I have walked the perimeter looking for any debris that fell to the ground. We picked up only a few little items. The perimeter looks good. I will terminate my daily air samples and will be leaving the site shortly.

**PRE-START VISUAL INSPECTION:**

**FINAL VISUAL INSPECTION:**


**PERIMETER INSPECTION:**

COMPLETED 08:30 HRS.

COMPLETED 12:15 HRS.

COMPLETED 11:30-12:00 HRS.

C:\Clients\Chicousd\PleasantValley senior High\R0726\062202DailyLog.wpd



Signature of Site Representative

**HAZARD MANAGEMENT SERVICES, INC.  
ASBESTOS ABATEMENT  
PRE-START VISUAL REPORT**

**CLIENT:** Chico USD

**HMS PROJECT #:** R0726

**CONTRACTOR:** Janus Corporation

**REMOVAL LOCATION:** Roof of shop building

**WORK TO BE CONDUCTED:** Removal of asbestos containing roofing materials around the perimeter edge of the roof only.

**PRE-START VISUAL INSPECTION RESULT**

**DATE:** 06/22/02

**FINDINGS:** Passed

**COMMENTS:** 09:00 hrs. - The contractor has successfully prepared the work area. Poly plastic sheeting is on the ground around the perimeter of the building. Barrier tape has been put into place. The waste bin is lined with 6mil poly plastic sheeting. Workers are donning protective coveralls and ½ mask HEPA filtered respirators. Worker documentation has been submitted. Contractor is ready to begin abatement.

C:\Clients\ChicoUSD\PleasantValley senior High\R0726\062202PreStartVis.wpd

  
Signature of HMS, Inc. Representative

**HAZARD MANAGEMENT SERVICES, INC.  
FINAL VISUAL CLEARANCE REPORT**

**CLIENT:** Chico USD

**HMS PROJECT #:**R0726

**CONTRACTOR:** Janus Corporation

**REMOVAL LOCATION:** Roof of the shop building

**WORK CONDUCTED:** Removal of asbestos containing roofing materials (ACM) from the entire perimeter roof edge of the shop building.

**FINAL VISUAL INSPECTION RESULT**

**DATE:** June 22, 2002

**FINDINGS:** Passed

**COMMENTS:** 12:15 hrs.- The contractor has removed the specified materials from the correct location. All waste generated by the removal work has been properly disposed of in a lined end dump located on the east side of the shop building. The contractor has completed the removal work.

C:\Clients\Chicousd\PleasantValley senior High\R0726\062202FinVis.wpd

  
\_\_\_\_\_  
Signature of HMS, Inc. Representative

# VISUAL INSPECTION OF EXTERIOR SCHOOL GROUNDS FOR ROOFING DEBRIS

Pleasant Valley Senior High School


## ROOFING PROJECT

INSPECTED BY: Cory Sanders

DATE: June 22, 2002

UNIT/WING	ROOM #/TIME	COMMENTS
Shop Building	11:30 hours	All debris has been picked up from around the shop building.

C:\Clients\Chicousd\PleasantValley senior High\R0726\062202ExtInsp.wpd



HMS, Inc. Representative Signature

**HAZARD MANAGEMENT SERVICES, INC.  
SITE REPRESENTATIVE'S DAILY LOG**

**Client:** Chico Unified School District  
**Project:** Pleasant Valley High School, T-1 Restroom Roofing

**Contact:** Rob Peters  
**Contact Phone:**  
**Contact Fax:**

**Project Number:** R0747

**Date:** July 29, 2002      **Day:** Monday      **Site Representative:** Robert Howell

**Abatement Contractor:** Janus Corporation  
**Abatement Supervisor:** Sergio Oseguera

**Contractor Phone:** (925) 313-8400  
**Contractor FAX:** (925) 370-0154

**Samples Collected:**      TEM - 0      PCM - 0      PLM - 0      Other - 0

**Number of Abatement Personnel:** 1 + 3

**Start Time:** 0930 hrs.      **End Time:** 1300 hrs.

**No. & Type of Waste Container(s):** Double six mil poly bags and "Burrito" wrapping.

**Scope Of Work:**

The removal of approximately 450 square feet of roofing material from the student restrooms building adjacent to Portable T-1.

0930 hrs. - Arrived on site, Janus on site with 1 supervisor and three crewmen. I introduced myself to Sergio and we both inspected the roofing to be removed from the restroom. The roofing material consist of a white rubberized canvas cap sheet over a white paper like base layer, roofing mastic has been applied at various locations on the roof, maybe 4 sq. ft. total. A portion of the cap sheet had been removed prior to my arrival, Janus crew is still setting up poly drop sheets.

1000 hrs. - Janus has completed set up, drop sheets and caution tape in place around the perimeter of the building, warning sign in place at access ladder. I gave permission to begin removal.

1020 hrs. - I called Kip Hanson with the District to confirm which of the materials on the roof contain asbestos, I assumed only the roofing mastic. He checked the lab results and believes the paper like backing is asbestos containing. I explained that if this is so, this material would be considered to be RACM by the EPA and therefore require a 10 day notification prior to removal. He explained he had talked with Rick Beall, of our office, and did not think there was a problem. I told him I would contact Rick and get some clarification.

1030 hrs. - Janus will fax employee documentation to our office, all current. The crew is thoroughly wetting the roofing material and hand scraping the remaining cap sheet material from the substrate. Due to fact that a majority of the paper backing was exposed prior to our arrival on site, I will allow the removal rather than leave the exposed material in place.

1045 hrs. - Janus has decided that rather than try to scrape the paper backing off the plywood substrate they would remove the plywood sheets with the paper intact, wrap the sheets in six mil poly and properly dispose of them. I spoke with Rick Beall and explained my concerns about which materials on this roof contain asbestos. He was unaware of any special conditions involving the roofing materials. I further explained that the material was being removed intact with the roof sheeting and I felt it was better to remove it now rather than wait and collect clarification bulk samples, he agreed.

  
\_\_\_\_\_  
Signature of Site Representative

**HAZARD MANAGEMENT SERVICES, INC.  
SITE REPRESENTATIVE'S DAILY LOG**

**Client:** Chico Unified School District  
**Project:** Pleasant Valley High School, T-1 Restroom Roofing

**Contact:** Rob Peters  
**Contact Phone:**  
**Contact Fax:**

**Project Number:** R0747

**Date:** July 29, 2002    **Day:** Monday    **Site Representative:** Robert Howell

1120 hrs. - Pre-wetted roof sheeting is coming up easily, no visible emissions from the work.

1200 hrs. - Plywood sheeting has been removed and wrapped for disposal, Janus crew is now pulling nails and HEPA vacuuming cracks, crevices, and surfaces in the now exposed ceiling cavity.

1215 hrs. - Janus requests final visual inspection of the roof work area.

1245 hrs. - The roof and the surrounding area are free from roofing debris, dust, and dirt. Final visual is successfully completed.

1300 hrs. - Janus crew packing up their tools and equipment, I left site.

**PRE-START VISUAL INSPECTION(s):**  
**FINAL VISUAL INSPECTION(s):**

COMPLETED 1000 HRS.  
COMPLETED 1245 HRS.


C:\Clientel\ChicoUSD\R0747PVValleyHS\072802Log.wpd

  
\_\_\_\_\_  
Signature of Site Representative



Current  
MAP  
5-15-01  
SANDERS  
COPY

Not on site  
at time of  
inspection



Student Parking Lot

ASBESTECH  
6825 Fair Oaks Blvd., Suite 103  
Carmichael, California 95608  
Tel.(916) 481-8902 Fax (916) 481-3975

***Client:***

Hazard Management Services  
4200 Rocklin Rd., Suite 11A  
Rocklin, CA 95677

***Job:***

R0726 Chico USD  
Pleasant Valley Senior HS  
Chico, Ca

**FIBER COUNT ANALYSIS REPORT**


LAB JOB # 40377  
Date Received: 6/24/02

PAT # 101801  
Date Reported: 6/24/02

<u>Date</u>	<u>Sample No.</u>	<u>Liters/Min.</u>	<u>Time Min.</u>	<u>Fibers</u>	<u>Fields</u>	<u>Fibers/CC</u>	<u>Det. Limit</u>	<u>TWA</u>
HMS-R0726-								
6/22/02	01	7.82	195	9.0	100	0.003	0.002	
East side of shop bldg. next to waste bin during roof removal								
6/22/02	02	7.82	180	3.0	100	<0.002	0.002	
East side of shop bldg. next to entrance gate during roof removal								

THE ANALYSIS USES PHASE CONTRAST MICROSCOPY AS DESCRIBED IN NIOSH METHOD 7400A. SAMPLES WERE NOT COLLECTED BY ASBESTECH. THIS REPORT MUST NOT BE REPRODUCED EXCEPT IN FULL WITH THE APPROVAL OF ASBESTECH. THIS REPORT RELATES ONLY TO THE ITEMS TESTED. ASBESTECH ACCEPTS TECHNICAL RESPONSIBILITY FOR THIS REPORT AND DATE OF ISSUE.

ANALYST SIGNATURE



**AIRBORNE FIBER** Analysis Request Form for Hazard Management Services, Inc.

4200 Rocklin Road, Suite 11A  
Rocklin, CA 95677  
(916) 632-6800  
FAX (916) 632-6841

**JOB I.D.:** R0726      **CLIENT:** Chico USD**COLLECTED BY:** Cory Sanders**DATE COLLECTED:** 06/22/02**DATE SUBMITTED:** 06/22/02**LAB SUBMITTED TO:** Asbestech**SPECIAL INSTRUCTIONS:** Please fax results to HMS and to the Chico USD at (530)891-3190 Attn: Rob Peters**ANALYSIS REQUESTED:** PCM**TURNAROUND TIME:** By 13:00 hours on  
06/25/02.

**JOB SITE:** Pleasant Valley Senior High School  
1475 East Avenue  
Chico, CA 95926

Sample#	Location Activity Date Collected	Rota	LPM	On/Off	Vol. (L)
			AVG.	Total	
HMS- R0726-01	East Side of Shop Building Next to Waste Bin During Roof Removal 06/22/02	HV- 21	7.82	09:00 hrs.	1,524.90
			7.82	12:15 hrs.	
			7.82	195 min.	
HMS- R0726-02	East Side of Shop Building Next to Entrance Gate During Roof Removal 06/22/02	HV- 21	7.82	09:15 hrs.	1,407.60
			7.82	12:15 hrs.	
			7.82	180 min.	

C:\Clients\ChicoUSD\Pleasant Valley senior High\R0726\AirClearanceRequest.wpd

**Delivered by:***Cory Sanders***Date:***06/24/02**OK 6/24/2; 11:50 a.m.*

## Rotameter Calibration Documentation

Manufacturer: Cole Parmer

Rotameter Number: HV-21

Date of Calibration: 02-11-02

City and Elevation: Sacramento, CA (<300 feet above sea level)

Temperature: 70°F

BIOS, DryCal, DC-Lite, Serial Number 3518, Model Number DCL-H Rev. 1.08

Calibrated By:

Signature


ROTAMETER READING (SCALE READING)	MINI-BUCK CALIBRATOR (LITERS/MINUTE)
15	3.66
20	5.13
30	7.82
40	10.65
50	13.57
56	15
60	16.39
70	19.42
80	22.25
90	25.40
99	28.3
100	28.36
104	29.45

ROTA	LPM
15	3.66
20	5.13
30	7.82
40	10.65
50	13.57
56	15
60	16.39
70	19.42
80	22.25
90	25.40
99	28.3
100	28.36
104	29.45

Calibrated 02-11-02  
HV-21  
Read Middle of Float  
Property of HMS, Inc.


Calibrated 02-11-02  
HV-21  
Read Middle of Float  
C:\RotameterHV21.wpd

**ROTAMETER CALIBRATION**  
Calibrated 02/11/02 - HV-21


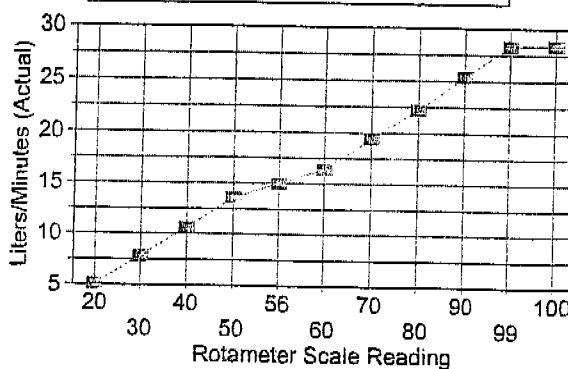


# ROTAMETER CALIBRATION

Calibrated 02/11/02 - HV-21

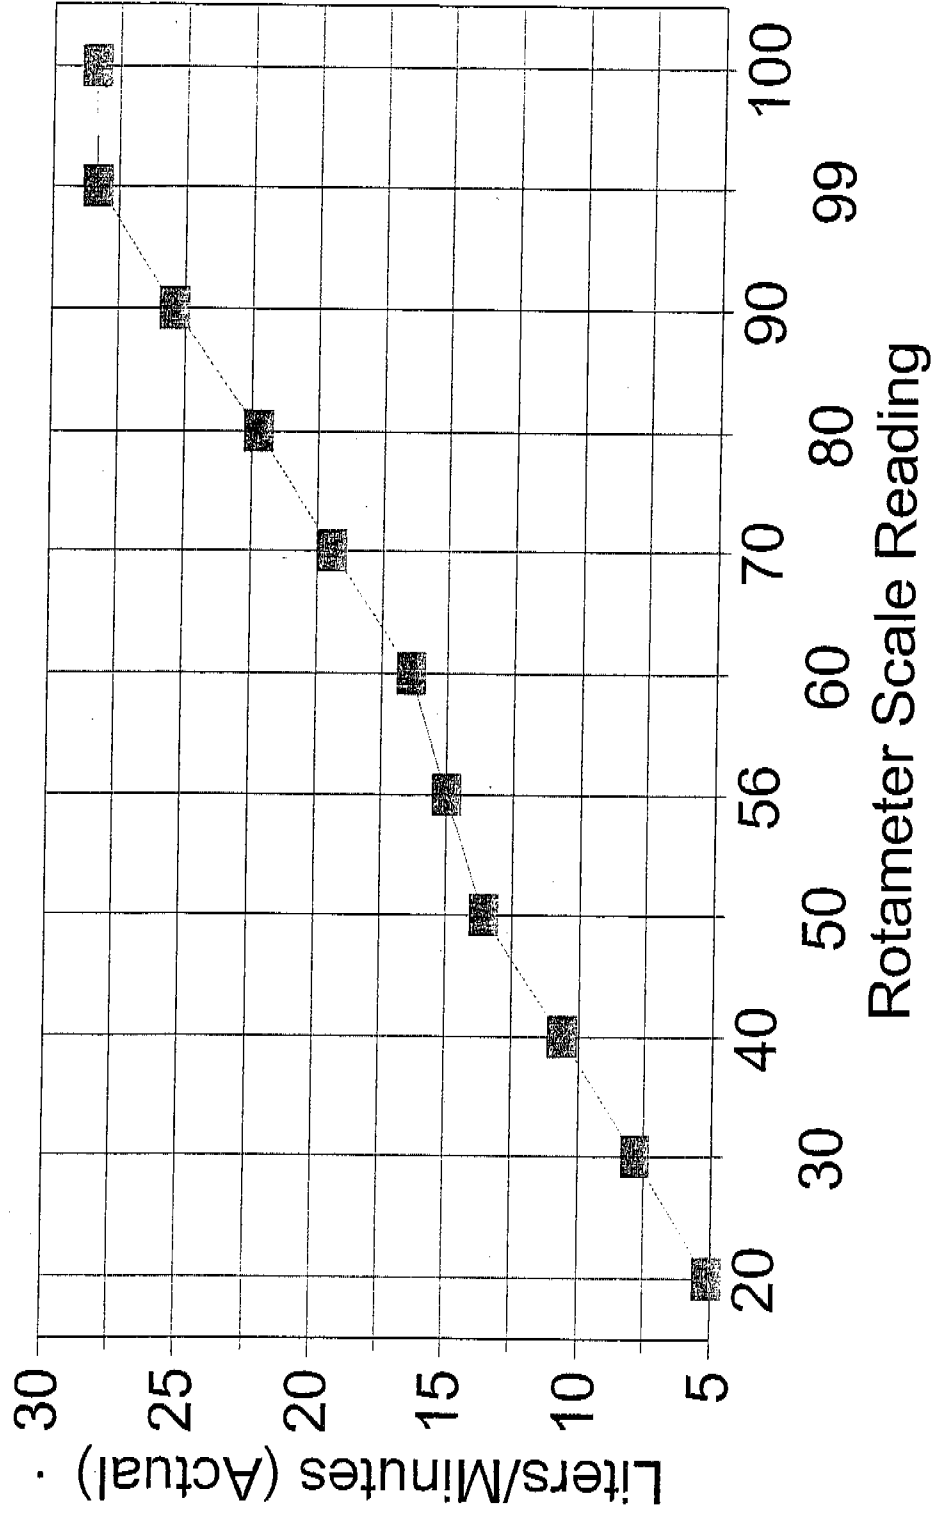

United States Department of Commerce  
National Institute of Standards and Technology



ISO/IEC 17025:1999  
ISO 9002:1994

## Certificate of Accreditation

**ASBESTECH**  
CARMICHAEL, CA

is recognized by the National Voluntary Laboratory Accreditation Program  
for satisfactory compliance with criteria set forth in NIST Handbook 150:2001,  
all requirements of ISO/IEC 17025:1999, and relevant requirements of ISO 9002:1994.  
Accreditation is awarded for specific services, listed on the Scope of Accreditation, for:

### AIRBORNE ASBESTOS FIBER ANALYSIS

June 30, 2003

Effective through

*David F. Alderman*

For the National Institute of Standards and Technology

NVLAP Lab Code: 101442-0

101801

PROFICIENCY ANALYTICAL TESTING (PAT) PROGRAM  
 INDIVIDUAL LABORATORY REPORT FOR ROUND 149  
 LAB ID#101801 MAY 8, 2002  
 ASBESTECH, CARMICHAEL, CA 95608

CONTAMINANT (ABV.)	UNIT	SAMPLE NO.	REPORTED RESULTS	MEAN VALUES *	ACCEPTABLE RANGE# LOWER	UPPER	Z & SCORE	LAB @ PERFORMANCE
ASBESTOS/FIBERS (ASB/MMF)	(F/MM2)	1	296.3000	294.0142	144.0670	496.8840	0.04	A
	(F/MM2)	2	284.2000	269.9045	132.2532	456.1385	0.26	A
	(F/MM2)	3	271.1000	316.0364	154.9658	534.4394	-0.74	A
	(F/MM2)	4	85.4000	81.2469	39.8110	137.3073	0.25	A

\* Mean values are the mean of all laboratories based on original scales except for asbestos. Asbestos results are calculated based on transformed data. Therefore, asbestos performance limits are not symmetrical to the mean values.  
 # Upper limit: mean value + 3 standard deviations  
 Lower limit: mean value - 3 standard deviations  
 & Z Score = (reported result - mean value) / standard deviation  
 @ A: Analysis acceptable      -: Results not reported  
 H: Results > upper limit (Z > 3), not acceptable      L: Results < lower limit (Z < -3), not acceptable  
 Note: the acceptability of reported results is based on z-scores. This is why a reported result may appear acceptable according to performance limits, but be identified as an outlier.

# University of California, Berkeley

## UNIVERSITY EXTENSION

This is to confirm that

Richard A. Beall


has attended the eight hour

AHERA Refresher Course for Asbestos Abatement Project Designers

and has completed the requisite training for asbestos accreditation under TSCA Title II

November 9, 2001

Certificate number: 3  
Valid until: November 9, 2002  
Cal/OSHA approval number: CA-002-10



*Richard V. Tsina*

Richard V. Tsina  
Chair, Environmental Management  
UC Berkeley Extension  
1995 University Avenue  
Berkeley, CA 94720  
(510) 643-7143



## DEPARTMENT OF INDUSTRIAL RELATIONS

## DIVISION OF OCCUPATIONAL SAFETY AND HEALTH

## ASBESTOS CONSULTANT and TRAINER APPROVAL UNIT

2 Park Towne Circle, Suite 1  
Sacramento, CA 95825  
(916) 574-2993 Fax (916) 483-0572



107262991T

225

8/28/2001

Cory Ryan Sanders  
Hazard Management Services, Inc  
4200 Rocklin Rd., Ste. 11A  
Rocklin, CA 95677

Dear Certified Asbestos Consultant or Technician:

Enclosed is your certification card. **To maintain your certification, please abide by the rules printed on the back of the certification card.**

Your certification is valid for a period of one year. If you wish to renew your certification, you must apply for renewal at least 60 days before the expiration date shown on your card. [8CCR 3205(h)(1)].

Please hold and do not send copies of your required AHERA refresher renewal certificates to the Division until you apply for renewal of your certification.

Please inform the Division of any changes in your mailing address or work address within 15 days.

Sincerely,

Rick Axe  
Senior Industrial Hygienist.

RA/dor

Attachment Cert. Card  
Reminder Notice

cc File

Cardltr.7/01

State of California  
Division of Occupational Safety and Health  
Certified Site Surveillance Technician  
**Cory Ryan Sanders**



Name

91-2991

Certification No.

8/15/2002

Expires on

This certification was issued by the Division of Occupational Safety and Health as authorized by Sections 7180 et seq. of the Business and Professions Code.
