Shasta Elementary

THREE-YEAR REINSPECTION

				CDS CODE 04-61424-6003099	
SCHOOL Shasta Elementary S	chool			SCHOOL PHONE NUMBER (530) 891-3141	
ADDRESS 169 Leora Court	(NUMBER)	(STREET)	(CITY) Chico, CA	(ZIP) 95973	

-IMPORTANT-

Each building and functional space with friable ACBM or friable assumed ACBM listed on this form requires completion of <u>FORM C</u> (PHYSICAL AND HAZARD ASSESSMENT OF FRIABLE ACBM OR FRIABLE ASSUMED ACBM). Indicate location of material on blueprint, diagram or narrative in square or linear feet, and attach a copy (Sec. 763.93).

		CHI	ECK O	NE		CHEC	K ONE	
LINE	BUILDING NAME & FUNCTIONAL SPACE	SUR-			AC	вм	ASSUME	D ACBM
	(Indicate Address if Different From Above)	FACING	TSI	MISC	FRIABLE	NON- FRIABLE	FRIABLE	NON- FRIABLE
1.	A - MPR - CERTIFICATION LETTER ON FILE DATED 11-1-01							
2.	B - CLASSROOMS 3, 6, & 7			Х		Х		Х
3.	C - CLASSROOMS 4, 5, & 8-10	X		Х		Х		Х
4.	D - PORTABLES 13, 13A, & 14			Х				Х
5.	E - CLASSROOM 15			Х				Х
6.	F - CLASSROOM 16			Х				Х
7.	G - CLASSROOM 17			Х				Х
8.	H - CLASSROOMS 19-21 - CERTIFICATION LETTER ON FILE DATED 9-24-97							
9.	I - CLASSROOMS 22 & 23 CERTIFICATION LETTER DATED 8-19-98							
10.	J - CLASSROOM 24 - CERTIFICATION LETTER DATED 8-19-98							
11.	K - CLASSROOM 18 CERTIFICATION LETTER DATED 9-24-97							
12.	L - CLASSROOMS 11 & 12 - CERTIFICATION LETTER ON FILE							
13.	M - ROOMS 920 & 921 - CERTIFICATION LETTER ON FILE							

Z:\Clients\Chico USD\13-2751 3 Year Reinspections\Sites\Shasta ES\Shasta Form B.wpd

See attached "Homogeneous Materials Records" for all materials and their locations by building. On Form B all buildings are listed, and a summary of all non-friable and friable material is provided. Friable materials and their locations are listed separately under each building on Form B.

District: Chico Unified School District

Inspector: Blake Howes

School: Shasta Elementary School Building: B - Classrooms 3, 6, & 7

Material Class	Material	Homo. Mat. #	% Asb.	Ft²/L.F.	Location	Condition	n: Code & Comments	Friable Yes/No
М	2' X 4' CEILING PANELS	1	NONE DETECTED	4,500 S	LIBRARY (922) AND CLASSROOMS 3, 6, AND 7	(13)	REPRESENTED BY SAMPLE HMS-SHA-01 COLLECTED IN 1988.	N/A
М	12" VINYL FLOOR TILE BEIGE	2	TRACE	2,500 S	ENTIRE WING	(1) (4)		N
М	DRYWALL	80	ASSUMED POSITIVE	1,500 S	ENTIRE WING	(11)	COVERED WITH TAGBOARD.	N
М	CEMENTITIOUS TRANSITE PANEL	99	ASSUMED POSITIVE	100 S	OUTSIDE BUILDING ABOVE DOORS AT COVERED WALKWAYS	(1) (4)		N
М	COVE BASE ADHESIVE	150	ASSUMED POSITIVE	500 L	LIBRARY, CLASSROOMS 3, 6 & 7	(1) (4)		N
М	CARPET ADHESIVE	151	ASSUMED POSITIVE	5,000 S	LIBRARY, CLASSROOMS 3, 6 & 7	(1) (4)		N

Z:\Clients\Chico USD\13-2751 3 Year Reinspections\Sites\Shasta ES\Shasta HMR.wpd

Date of Inspection: August 6, 2013

CONDITION CODE

General Condition: (1) Good (2) Damaged (3) Significantly Damaged (25% or more)

<u>Change in Condition:</u> (4) No (5) Yes (If Yes, explain under comments)

Abated: (6) Repaired (7) Removed (8) Encapsulated (9) Enclosed (10) Isolated & Restricted

Miscellaneous: (11) Inaccessible, no inspection data (12) Other (Explain under comments) (13) Non-Asbestos/Not Inspected

District: Chico Unified School District

Inspector: Blake Howes

School: Shasta Elementary School Building: C - Classrooms 4, 5, & 8-10

Material Class	Material	Homo. Mat. #	% Asb.	Ft²/L.F.	Location	Conditio	n: Code & Comments	Friable Yes/No
М	2 X 4 CEILING PANELS FISSURE PATTERN	1	NONE DETECTED	7,000 S	OFFICE (915) AND CLASSROOMS 4, 5, 8, 9 AND 10	(13)	SAMPLE HMS-SHA-01 COLLECTED IN 1988.	N/A
М	12" VINYL FLOOR TILE(CREAM) & ADHESIVE	2	TRACE	600 S	OFFICE (915) AN D PRINCIPAL OFFICE	(1) (4) (11)	CARPET OVER TILE IN PRINCIPAL OFFICE.	N
S	PLASTER	86	ASSUMED POSITIVE	250 S	MEN'S (912) & WOMEN'S (914) RESTROOM CEILINGS	(1) (4)		N
М	CEMENTITIOUS TRANSITE PANELS	99	ASSUMED POSITIVE	200 S	ABOVE DOORS AT COVERED WALKWAYS	(1) (4)		N
М	DRYWALL	112	ASSUMED POSITIVE	5,000 S	THROUGHOUT OFFICES & CLASSROOMS	(11)	COVERED WITH TAGBOARD IN ALL CLASSROOMS - NOT INSPECTED	N
М	COVE BASE ADHESIVE	150	ASSUMED POSITIVE	700 L	THROUGHOUT OFFICES & CLASSROOMS	(1) (4)		N
М	CARPET ADHESIVE	151	ASSUMED POSITIVE	5,000 S	THROUGHOUT OFFICES & CLASSROOMS	(1) (4)		N

Z:\Clients\Chico USD\13-2751 3 Year Reinspections\Sites\Shasta ES\Shasta HMR.wpd

Date of Inspection: August 6, 2013

CONDITION CODE

General Condition: (1) Good (2) Damaged (3) Significantly Damaged (25% or more)

Change in Condition: (4) No (5) Yes (If Yes, explain under comments)

Abated: (6) Repaired (7) Removed (8) Encapsulated (9) Enclosed (10) Isolated & Restricted

Miscellaneous: (11) Inaccessible, no inspection data (12) Other (Explain under comments) (13) Non-Asbestos/Not Inspected

District: Chico Unified School District

Inspector: Blake Howes

School: Shasta Elementary

Building: D - Portables 13, 13A, & 14

Material Class	Material	Homo. Mat. #	% Asb.	Ft²/L.F.	Location	Condition: Code & Comments	Friable Yes/No
М	2' X 4' CEILING PANELS FIBERGLASS	60	NON- SUSPECT	2,200 S	PORTABLES 13, 13A, AND 14	(13)	N/A
М	12" VINYL FLOOR TILE (WHITE) & ADHESIVE	70	ASSUMED POSITIVE	2,300 S	PORTABLES 13, 13A, AND 14	(11) ASSUMED POSITIVE TO EXIST BENEATH CARPET	N
М	COVE BASE ADHESIVE	150	ASSUMED POSITIVE	325 L	PORTABLES 13, 13A, AND 14	(1) (4)	N
М	CARPET ADHESIVE	151	ASSUMED POSITIVE	1,650 S	PORTABLES 13, 13A, AND 14	(1) (4)	N
						ROOM 14 - DESIGNATED MOBILE SYSTEMS IND. 7/01 SERIAL # 20.1083.1 & 2 ROOM 13 - DESIGNATED MOBILE SYSTEMS IND. 7/01 SERIAL # 20.1084 # 3 & # 2 DESIGNATED MOBILE SYSTEMS IND. 7/01 SERIAL # 20.1084 # 1	

Z:\Clients\Chico USD\13-2751 3 Year Reinspections\Sites\Shasta ES\Shasta HMR.wpd

Date of Inspection: August 6, 2013

CONDITION CODE

General Condition: (1) Good (2) Damaged (3) Significantly Damaged (25% or more)

<u>Change in Condition:</u> (4) No (5) Yes (If Yes, explain under comments)

Abated: (6) Repaired (7) Removed (8) Encapsulated (9) Enclosed (10) Isolated & Restricted

Miscellaneous: (11) Inaccessible, no inspection data (12) Other (Explain under comments) (13) Non-Asbestos/Not Inspected

District: Chico Unified School District

Inspector: Blake Howes

School: Shasta Elementary School

Building: E - Classroom 15

Material Class	Material	Homo. Mat. #	% Asb.	Ft²/L.F.	Location	Condition: Code & Comments	Friable Yes/No
М	12" VINYL FLOOR TILE (TAN) & ADHESIVE	109	ASSUMED POSITIVE	253 S	CLASSROOM 15	(1) (4)	N
М	2' X 4' CEILING PANELS FISSURE PATTERN	110	ASSUMED POSITIVE	900 S	CLASSROOM 15	(1) (4)	N
М	DRYWALL	111	ASSUMED POSITIVE	900 S	CLASSROOM 15	(11) DRYWALL BEHIND TAGBOARD.	N
М	COVE BASE ADHESIVE	150	ASSUMED POSITIVE	80 L	CLASSROOM 15	(1) (4)	N
М	CARPET ADHESIVE	151	ASSUMED POSITIVE	375 S	CLASSROOM 15	(1) (4)	N
						BUILT BY HUFFMAN - AUG. 1987 - NO SERIAL #	

Z:\Clients\Chico USD\13-2751 3 Year Reinspections\Sites\Shasta ES\Shasta HMR.wpd

Date of Inspection: August 6, 2013

CONDITION CODE

General Condition: (1) Good (2) Damaged (3) Significantly Damaged (25% or more)

Change in Condition: (4) No (5) Yes (If Yes, explain under comments)

Abated: (6) Repaired (7) Removed (8) Encapsulated (9) Enclosed (10) Isolated & Restricted

Miscellaneous: (11) Inaccessible, no inspection data (12) Other (Explain under comments) (13) Non-Asbestos/Not Inspected

District: Chico Unified School District

Inspector: Blake Howes

School: Shasta Elementary School Building: F - Classroom 16

Material Class	Material	Homo. Mat. #	% Asb.	Ft²/L.F.	Location	Condition: Code & Comments	Friable Yes/No
М	12" VINYL FLOOR TILE (TAN) & ADHESIVE	109	ASSUMED POSITIVE	253 S	CLASSROOM 16	(1) (4)	N
М	2' X 4' CEILING PANELS	110	ASSUMED POSITIVE	900 S	CLASSROOM 16	(1) (4)	N
М	DRYWALL	111	ASSUMED POSITIVE	900 S	CLASSROOM 16	(11) DRYWALL BEHIND TAGBOARD.	N
М	COVE BASE ADHESIVE	150	ASSUMED POSITIVE	120 L	CLASSROOM 16	(1) (4)	N
М	CARPET ADHESIVE	151	ASSUMED POSITIVE	900 S	CLASSROOM 16	(1) (4)	N
						BUILT BY: KRUSEMARK - JULY 1988 SERIAL # 8751-16 B & C	

Z:\Clients\Chico USD\13-2751 3 Year Reinspections\Sites\Shasta ES\Shasta HMR.wpd

Date of Inspection: August 6, 2013

CONDITION CODE

General Condition: (1) Good (2) Damaged (3) Significantly Damaged (25% or more)

Change in Condition: (4) No (5) Yes (If Yes, explain under comments)

Abated: (6) Repaired (7) Removed (8) Encapsulated (9) Enclosed (10) Isolated & Restricted

Miscellaneous: (11) Inaccessible, no inspection data (12) Other (Explain under comments) (13) Non-Asbestos/Not Inspected

District: Chico Unified School District

Inspector: Blake Howes

School: Shasta Elementary School Building: G - Classroom 17

Material Class	Material	Homo. Mat. #	% Asb.	Ft²/L.F.	Location	Condition: Code & Comments	Friable Yes/No
М	12" VINYL FLOOR TILE (TAN) & ADHESIVE	109	ASSUMED POSITIVE	253 S	CLASSROOM 17	(1) (4)	N
М	2' X 4' CEILING PANELS	110	ASSUMED POSITIVE	900 S	CLASSROOM 17	(1) (4)	N
М	DRYWALL	111	ASSUMED POSITIVE	900 S	CLASSROOM 17	(11) DRYWALL BEHIND TAGBOARD	N
М	COVE BASE ADHESIVE	152	ASSUMED POSITIVE	120 L	CLASSROOM 17	(1) (4)	N
М	CARPET ADHESIVE	151	ASSUMED POSITIVE	900 L	CLASSROOM 17	(1) (4)	N
						UNKNOWN MANUFACTURER - UNKNOWN BUILD DATE SERIAL # 8888.10 A & B	

Z:\Clients\Chico USD\13-2751 3 Year Reinspections\Sites\Shasta ES\Shasta HMR.wpd

Date of Inspection: August 6, 2013


CONDITION CODE

General Condition: (1) Good (2) Damaged (3) Significantly Damaged (25% or more)

<u>Change in Condition:</u> (4) No (5) Yes (If Yes, explain under comments)

Abated: (6) Repaired (7) Removed (8) Encapsulated (9) Enclosed (10) Isolated & Restricted

Miscellaneous: (11) Inaccessible, no inspection data (12) Other (Explain under comments) (13) Non-Asbestos/Not Inspected

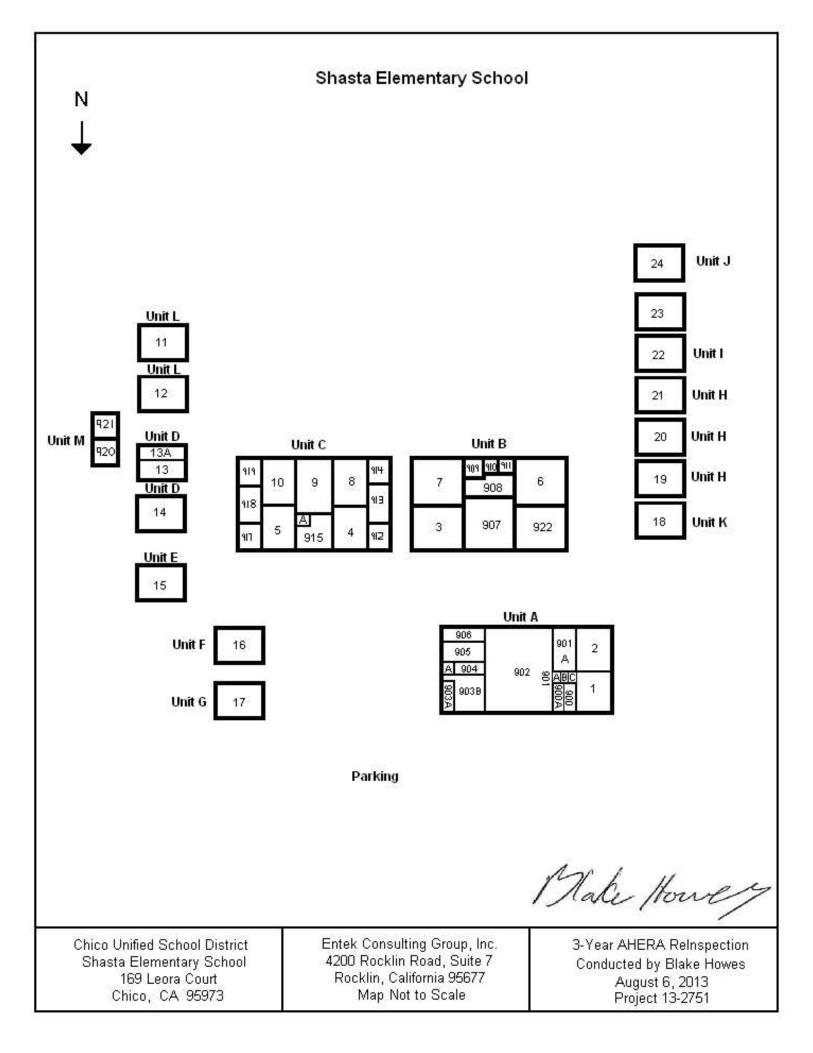

SIX-MONTH SURVEILLANCE	

SIX MONTH SURVEILLANCE HOMOGENEOUS ACBM RECORDS

Date of Inspection:

District: School:

Chico Unified School District Ins Shasta Elementary $\bf School$ $\bf Bu$

Material Class	Material	Homo. Mat. #	% Asb.	Ft²/L.F.	Location	Conditio	n: Code & Comments	Friable Yes/No
М	2' X 4' CEILING PANELS	1	NONE DETECTED	4,500 S	LIBRARY (922) AND CLASSROOMS 3, 6, AND 7	(13)	REPRESENTED BY SAMPLE HMS-SHA-01 COLLECTE D IN 1988.	N/A
М	12" VINYL FLOOR TILE BEIGE	2	TRACE	2,500 S	ENTIRE WING	(1) (4)		N
М	DRYWALL	80	ASSUMED POSITIVE	1,500 S	ENTIRE WING	(11)	COVERED WITH TAGBOARD.	N
М	CEMENTITIOUS TRANSITE PANEL	99	ASSUMED POSITIVE	100 S	OUTSIDE BUILDING ABOVE DOORS AT COVERED WALKWAYS	(1) (4)		N
М	COVE BASE ADHESIVE	150	ASSUMED POSITIVE	500 L	LIBRARY, CLASSROOMS 3, 6 & 7	(1) (4)		N
М	CARPET ADHESIVE	151	ASSUMED POSITIVE	5,000 S	LIBRARY, CLASSROOMS 3, 6 & 7	(1) (4)		N

 ${\tt Z:\Clients\Chico\ USD\13-2751\ 3\ Year\ Reinspections\Sites\Shasta\ ES\Shasta\ 6\ month.wpd}$

CONDITION CODE

General Condition: (1) Good (2) Damaged (3) Significantly Damaged (25% or more)

Change in Condition: (4) No (5) Yes (If Yes, explain under comments)

Abated: (6) Repaired (7) Removed (8) Encapsulated (9) Enclosed (10) Isolated & Restricted

Miscellaneous: (11) Inaccessible, no inspection data (12) Other (Explain under comments) (13) Non-Asbestos/Not Inspected

SIX MONTH SURVEILLANCE **HOMOGENEOUS ACBM RECORDS**

Date of Inspection:

District:

School:

Chico Unified School District Ins

Shasta Elementary School Bui

Material Class	Material	Homo. Mat. #	% Asb.	Ft²/L.F.	Location	Condition: Code & Comments	Friable Yes/No
М	2 X 4 CEILING PANELS FISSURE PATTERN	1	NONE DETECTED	7,000 S	OFFICE (915) AND CLASSROOMS 4, 5, 8, 9 AND 10	(13) SAMPLE HMS-SHA-01 COLLECTED IN 1988.	N/A
М	12" VINYL FLOOR TILE(CREAM) & ADHESIVE	2	TRACE	600 S	OFFICE (915) AN D PRINCIPAL OFFICE	(1) (4) (11) CARPET OVER TILE IN PRINCIPAL OFFICE.	N
S	PLASTER	86	ASSUMED POSITIVE	250 S	MEN'S (912) & WOMEN'S (914) RESTROOM CEILINGS	(1) (4)	N
М	CEMENTITIOUS TRANSITE PANELS	99	ASSUMED POSITIVE	200 S	ABOVE DOORS AT COVERED WALKWAYS	(1) (4)	N
М	DRYWALL	112	ASSUMED POSITIVE	5,000 s	THROUGHOUT OFFICES & CLASSROOMS	(11) COVERED WITH TAGBOARD IN ALL CLASSROOMS - NOT INSPECTED	N
М	COVE BASE ADHESIVE	150	ASSUMED POSITIVE	700 L	THROUGHOUT OFFICES & CLASSROOMS	(1) (4)	N
М	CARPET ADHESIVE	151	ASSUMED POSITIVE	5,000 s	THROUGHOUT OFFICES & CLASSROOMS	(1) (4)	N

Z:\Clients\Chico USD\13-2751 3 Year Reinspections\Sites\Shasta ES\Shasta 6 month.wpd

CONDITION CODE

(2) Damaged (3) Significantly Damaged (25% or more) General Condition: (1) Good

Change in Condition: (4) No (5) Yes (If Yes, explain under comments) Abated:

(6) Repaired (7) Removed (8) Encapsulated (9) Enclosed (10) Isolated & Restricted

(11) Inaccessible, no inspection data (12) Other (Explain under comments) Miscellaneous: (13) Non-Asbestos/Not Inspected CONSULT ORIGINAL AND SUPPLEMENTARY INSPECTION REPORTS FOR MATERIALS WITH TRACE AMOUNTS OF ASBESTOS

SIX MONTH SURVEILLANCE **HOMOGENEOUS ACBM RECORDS**

Date of Inspection:

District:

Chico Unified School District Ins

School:

Shasta Elementary Bui

Material Class	Material	Homo. Mat. #	% Asb.	Ft²/L.F.	Location	Condition: Code & Comments		
М	2' X 4' CEILING PANELS FIBERGLASS	60	NON- SUSPECT	2,200 S	PORTABLES 13, 13A, AND 14	(13)	N/A	
М	12" VINYL FLOOR TILE (WHITE) & ADHESIVE	70	ASSUMED POSITIVE	2,300 S	PORTABLES 13, 13A, AND 14	(11) ASSUMED POSITIVE TO EXIST BENEATH CARPET	N	
М	COVE BASE ADHESIVE	150	ASSUMED POSITIVE	325 L	PORTABLES 13, 13A, AND 14	(1) (4)	N	
М	CARPET ADHESIVE	151	ASSUMED POSITIVE	1,650 S	PORTABLES 13, 13A, AND 14	(1) (4)	N	
						ROOM 14 - DESIGNATED MOBILE SYSTEMS IND. 7/01 SERIAL # 20.1083.1 & 2 ROOM 13 - DESIGNATED MOBILE SYSTEMS IND. 7/01 SERIAL # 20.1084 # 3 & # 2 ROOM 13A - DESIGNATED MOBILE SYSTEMS IND. 7/01 SERIAL # 20.1084 # 1		

Z:\Clients\Chico USD\13-2751 3 Year Reinspections\Sites\Shasta ES\Shasta 6 month.wpd

CONDITION CODE

General Condition: (1) Good (2) Damaged (3) Significantly Damaged (25% or more)

Change in Condition: (4) No (5) Yes (If Yes, explain under comments)

Abated: (6) Repaired (7) Removed (8) Encapsulated (9) Enclosed (10) Isolated & Restricted

(11) Inaccessible, no inspection data (12) Other (Explain under comments) (13) Non-Asbestos/Not Inspected Miscellaneous:

SIX MONTH SURVEILLANCE HOMOGENEOUS ACBM RECORDS

Date of Inspection:

District:

Chico Unified School District Ins

Shasta Elementary School Bui

School:		

Material Class	Material	Homo. Mat. #	% Asb.	Ft²/L.F.	Location	Condition: Code & Comments	Friable Yes/No
М	12" VINYL FLOOR TILE (TAN) & ADHESIVE	109	ASSUMED POSITIVE	253 S	CLASSROOM 15	(1) (4)	N
М	2' X 4' CEILING PANELS FISSURE PATTERN	110	ASSUMED POSITIVE	900 S	CLASSROOM 15	(1) (4)	N
М	DRYWALL	111	ASSUMED POSITIVE	900 S	CLASSROOM 15	(11) DRYWALL BEHIND TAGBOARD.	N
M	COVE BASE ADHESIVE	150	ASSUMED POSITIVE	80 L	CLASSROOM 15	(1) (4)	N
М	CARPET ADHESIVE	151	ASSUMED POSITIVE	375 S	CLASSROOM 15	(1) (4)	N
						BUILT BY HUFFMAN - AUG. 1987 - NO SERIAL #	

Z:\Clients\Chico USD\13-2751 3 Year Reinspections\Sites\Shasta ES\Shasta 6 month.wpd

CONDITION CODE

General Condition: (1) Good (2) Damaged (3) Significantly Damaged (25% or more)

Change in Condition: (4) No (5) Yes (If Yes, explain under comments)

Abated: (6) Repaired (7) Removed (8) Encapsulated (9) Enclosed (10) Isolated & Restricted

Miscellaneous: (11) Inaccessible, no inspection data (12) Other (Explain under comments) (13) Non-Asbestos/Not Inspected

SIX MONTH SURVEILLANCE **HOMOGENEOUS ACBM RECORDS**

Date of Inspection:

Chico Unified School District Ins

Shasta Elementary School Bui

District: School:

Material Class	Material	Homo. Mat. #	% Asb.	Ft²/L.F.	Location	Condition: Code & Comments	Friable Yes/No
М	12" VINYL FLOOR TILE (TAN) & ADHESIVE	109	ASSUMED POSITIVE	253 S	CLASSROOM 16	(1) (4)	N
М	2' X 4' CEILING PANELS	110	ASSUMED POSITIVE	900 S	CLASSROOM 16	(1) (4)	N
М	DRYWALL	111	ASSUMED POSITIVE	900 S	CLASSROOM 16	(11) DRYWALL BEHIND TAGBOARD.	N
М	COVE BASE ADHESIVE	150	ASSUMED POSITIVE	120 L	CLASSROOM 16	(1) (4)	N
М	CARPET ADHESIVE	151	ASSUMED POSITIVE	900 S	CLASSROOM 16	(1) (4)	N
						BUILT BY: KRUSEMARK - JULY 1988 SERIAL # 8751-16 B & C	

Z:\Clients\Chico USD\13-2751 3 Year Reinspections\Sites\Shasta ES\Shasta 6 month.wpd

CONDITION CODE

General Condition: (2) Damaged (3) Significantly Damaged (25% or more) (1) Good

Change in Condition: (4) No (5) Yes (If Yes, explain under comments)

Abated: (6) Repaired (7) Removed (8) Encapsulated (9) Enclosed (10) Isolated & Restricted

(11) Inaccessible, no inspection data (12) Other (Explain under comments) Miscellaneous: (13) Non-Asbestos/Not Inspected

SIX MONTH SURVEILLANCE HOMOGENEOUS ACBM RECORDS

Date of Inspection:

District:

School:

Chico Unified School District Ins

Shasta Elementary School Bui

Material Class	Material	Homo. Mat. #	% Asb.	Ft ² /L.F.	Location	Condition: Code & Comments	Friable Yes/No
М	12" VINYL FLOOR TILE (TAN) & ADHESIVE	109	ASSUMED POSITIVE	253 S	CLASSROOM 17	(1) (4)	N
М	2' X 4' CEILING PANELS	110	ASSUMED POSITIVE	900 S	CLASSROOM 17	(1) (4)	N
М	DRYWALL	111	ASSUMED POSITIVE	900 S	CLASSROOM 17	(11) DRYWALL BEHIND TAGBOARD	Ν
М	COVE BASE ADHESIVE	152	ASSUMED POSITIVE	120 L	CLASSROOM 17	(1) (4)	N
М	CARPET ADHESIVE	151	ASSUMED POSITIVE	900 L	CLASSROOM 17	(1) (4)	N
						UNKNOWN MANUFACTURER - UNKNOWN BUILD DATE SERIAL # 8888.10 A & B	

 ${\tt Z:\Clients\Chico\ USD\13-2751\ 3\ Year\ Reinspections\Sites\Shasta\ ES\Shasta\ 6\ month.wpd}$

CONDITION CODE

General Condition: (1) Good (2) Damaged (3) Significantly Damaged (25% or more)

Change in Condition: (4) No (5) Yes (If Yes, explain under comments)

Abated: (6) Repaired (7) Removed (8) Encapsulated (9) Enclosed (10) Isolated & Restricted

Miscellaneous: (11) Inaccessible, no inspection data (12) Other (Explain under comments) (13) Non-Asbestos/Not Inspected
